


Wastewater Utility 2020 Monthly Report



July 2020

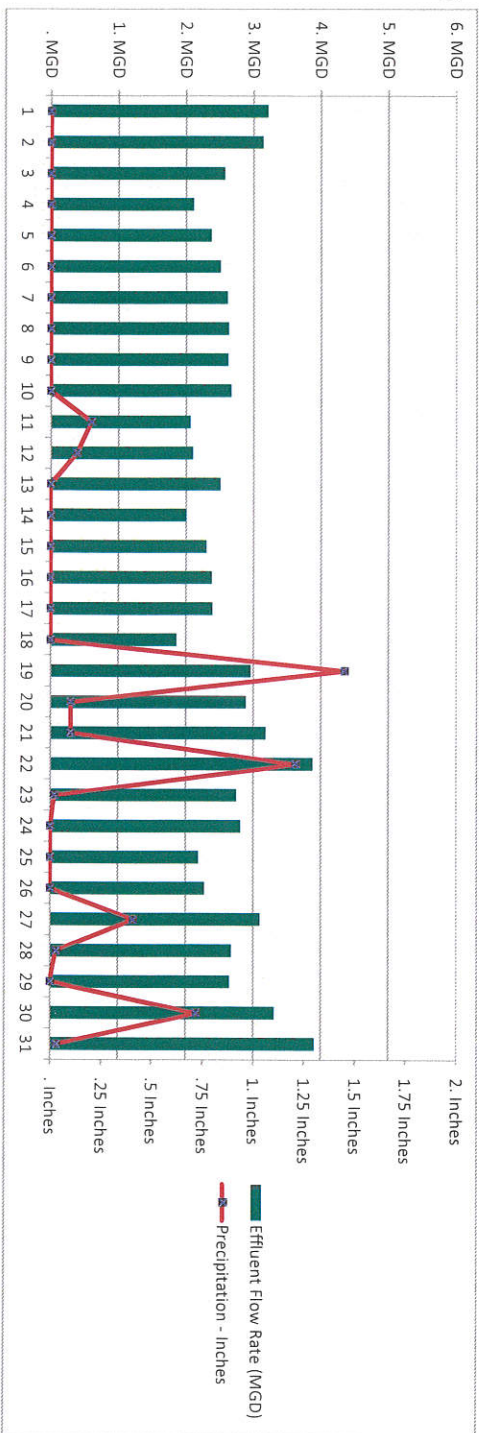

| Month | January | February | March | April | May | June | July | August | September | October | November | December | Total |
|--|---------|----------|--------|--------|--------|--------|-------|--------|-----------|---------|----------|----------|---------|
| Total MG Treated Effluent 2020 | 125.83 | 104.77 | 110.88 | 88.40 | 102.31 | 95.70 | 82.61 | | | | | | 710.5 |
| Total MG Treated Effluent 2019 | 123.30 | 138.30 | 122.91 | 154.54 | 127.04 | 152.68 | 92.70 | 78.41 | 62.48 | 68.74 | 69.23 | 107.24 | 1297.57 |
| Total Monthly Precipitation 2020 | 6.12 | 5.26 | 4.51 | 1.92 | 4.95 | 6.30 | 4.40 | | | | | | 33.46 |
| 2020 Monthly Percent Capacity Actual Design Flow 4.0 MGD | 101% | 90% | 89% | 74% | 83% | 80% | 67% | | | | | | 84% |

Sewer Crew Activities

1. Performed 33 lateral inspections
2. Completed routine maintenance and lift station checks.
3. Cleaned 4545' of storm and sanitary lines.
4. Responded to service calls
5. Cleaned and checked catch basins.
6. Repaired 3 storm catch basins.
7. Installed 200' of perforated pipe and 2 catch basins near the new brush/compost area.
8. Completed dirt work at several pervious work sites.
9. Installed new pumps at Fleming, Indigo Springs, and Greenfield Village lift stations.
10. Conducted video inspection of sanitary and storm lines throughout the systems.

Plant Crew Activities

- Sludge Pressed / Gallons: 599,500**
- Plant Operations and Maintenance:**
1. Completed required monthly maintenance.
 2. Maintenance project is near completion: waiting on some parts that were back ordered; also had some shipping issues.
 3. Replaced the overload and contactor on one of the conveyors in the headworks building.
 4. Replaced the check ball in primary sludge pump #2; had worn down and got stuck in the discharge pipe.
 5. Installed new air valve bodies on primary sludge pumps #2 and #4.
 6. Installed new air tanks on compressor in the C-Tech room.
 7. Repaired the shaft on the skimmer in clarifier #3; trusted through and broke off; able to have it welded back in place.
