


Wastewater Utility 2023 Monthly Report

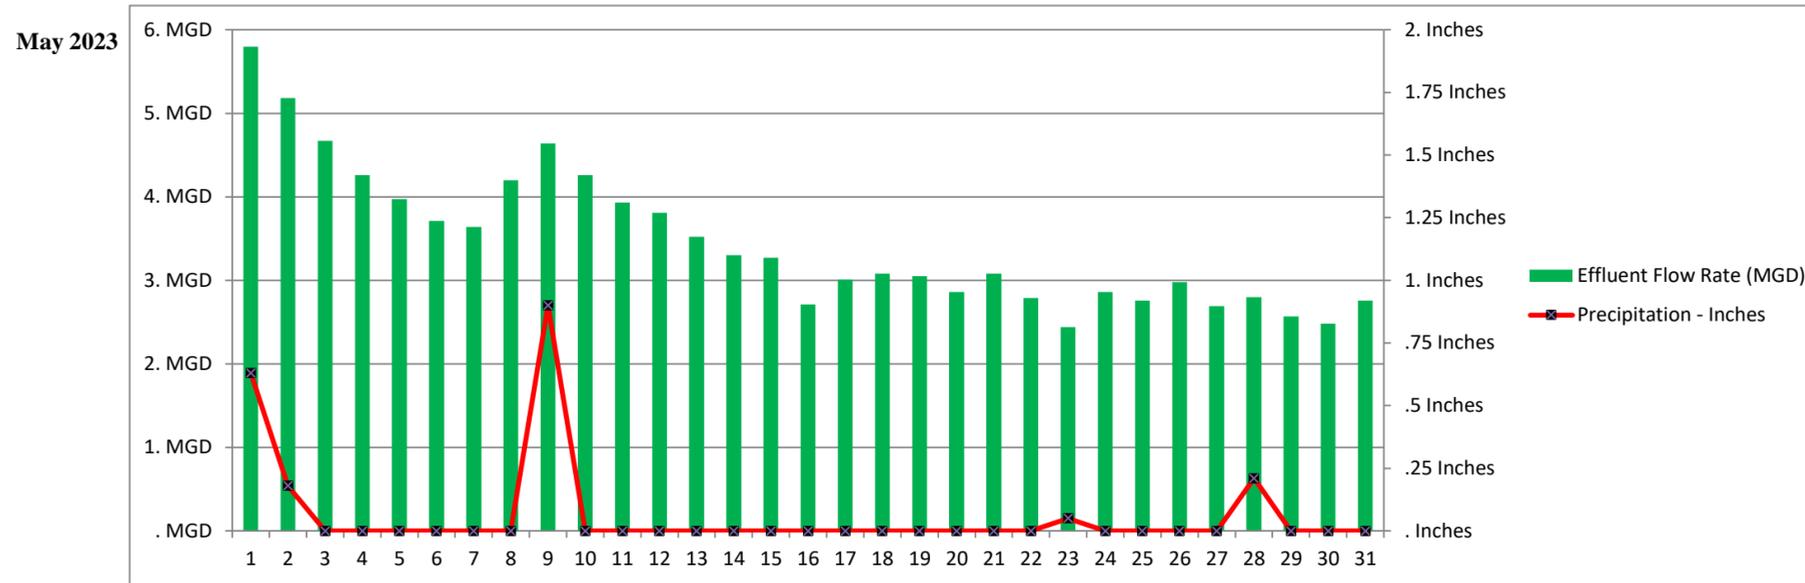

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2023	119.40	96.16	164.80	95.29	88.73								564.38
Total MG Treated Effluent 2022	107.08	132.88	140.54	120.85	123.71	86.77	72.59	84.83	81.02	69.45	67.96	77.22	1164.90
Total Monthly Precipitation 2023	3.40	2.29	7.39	2.40	1.32								16.80
Total Monthly Precipitation 2022	1.97	5.87	4.9	4.52	7.72	2.05	2.43	6.55	3.13	1.41	2.25	3.58	46.38
2023 Monthly Percent Capacity	96%	86%	133%	79%	72%								93%
Actual Design Flow 4.0 MGD													

Sewer Crew Activities	Plant Crew Activities
<ol style="list-style-type: none"> Performed 8 lateral inspections. Completed semi annual maintenance and lift station checks. Responded to 3 service calls: homeowners and lift stations. Cleaned and inspected 1090 feet of sanitary and 20 feet of storm mainlines. Repaired/replaced 20 feet of sanitary mains. Repaired/replaced 20 feet of storm mains. Installed 1 new storm structure. Repaired 10 storm structures. Completed site dirt work at various work sites. 	<p style="text-align: center;">Sludge Pressed / Gallons: 1,525,500</p> <p>Plant Operations and Maintenance:</p> <ol style="list-style-type: none"> Completed required monthly maintenance. Hauled out 12 tons of bio-solids. Capped 4" effluent suction line between contact tank and chemical building in prep for underground pipe install. Replaced pump heads on chemical feed pumps. Culy Contracting helped to repair a leak on one of the primary tank walls. Replaced motor on the fine screen. Maddox Industrial replaced the gear box on the headworks conveyor that failed in March.

Monthly Overtime					
WWTP Operators			Collection System Operators		
Scheduled: weekends, holidays	Emergency Call Ins	Other	Unscheduled	Emergency Call Ins	Other
42.25	14	0	14.5	24	0
Total Dept. Overtime:		94.75			
