


Wastewater Utility 2021 Monthly Report



February 2021

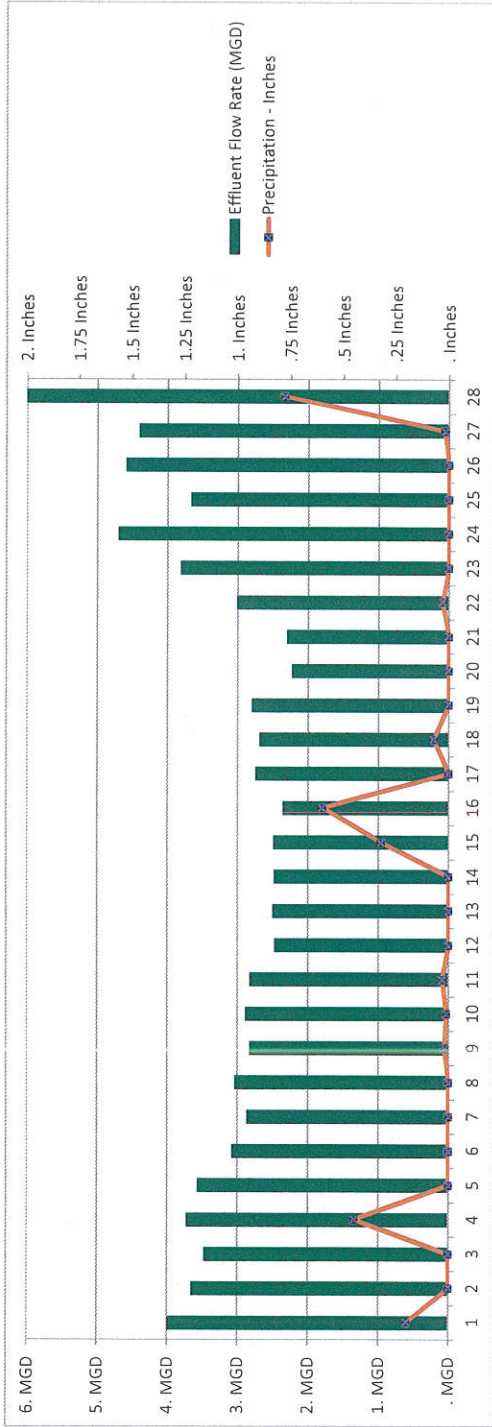

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2021	93.67	91.88											185.55
Total MG Treated Effluent 2020	125.83	104.77	110.88	88.40	102.31	95.70	82.61	83.06	64.78	80.31	90.43	83.15	1112.23
Total Monthly Precipitation 2021	2.91	2.53											5.44

2021 Monthly Percent Capacity	76%	82%											79%
Actual Design Flow 4.0 MGD													

Sewer Crew Activities

1. Performed 11 lateral inspections
2. Completed routine maintenance and lift station checks.
3. Cleaned and/or CCTV'd 2775' of sanitary and storm lines.
4. Responded to 8 service calls.
5. Helped with the snow removal the week of 2/15.
6. Started clearing trees and brush inside the construction limits for the new road and WWTP.
7. Replaced a sanitary lateral at 616 W. Michigan.
8. Hauled bio-solids to landfill for the WWTP.
9. Checked and cleaned storm catch basins.

Plant Crew Activities

Sludge Pressed / Gallons: 635,000

Plant Operations and Maintenance:

1. Completed required monthly maintenance.
2. Hauled out 497 tons of bio-solids. We had to send 142 tons to the landfill due to it not meeting our permit limits for Marketing and Distribution.
3. Replaced the check balls in primary sludge pump #4.
4. Had to make a temporary repair to the mixing auger in order to keep it running, the new unit has been delivered and we are planning to get it installed the week of March 22nd.
5. The rod on the skimmer in clarifier #4 broke and had to be welded back in place.
6. The high level float for our fine screen failed and had to be replaced.
