


Wastewater Utility 2021 Monthly Report

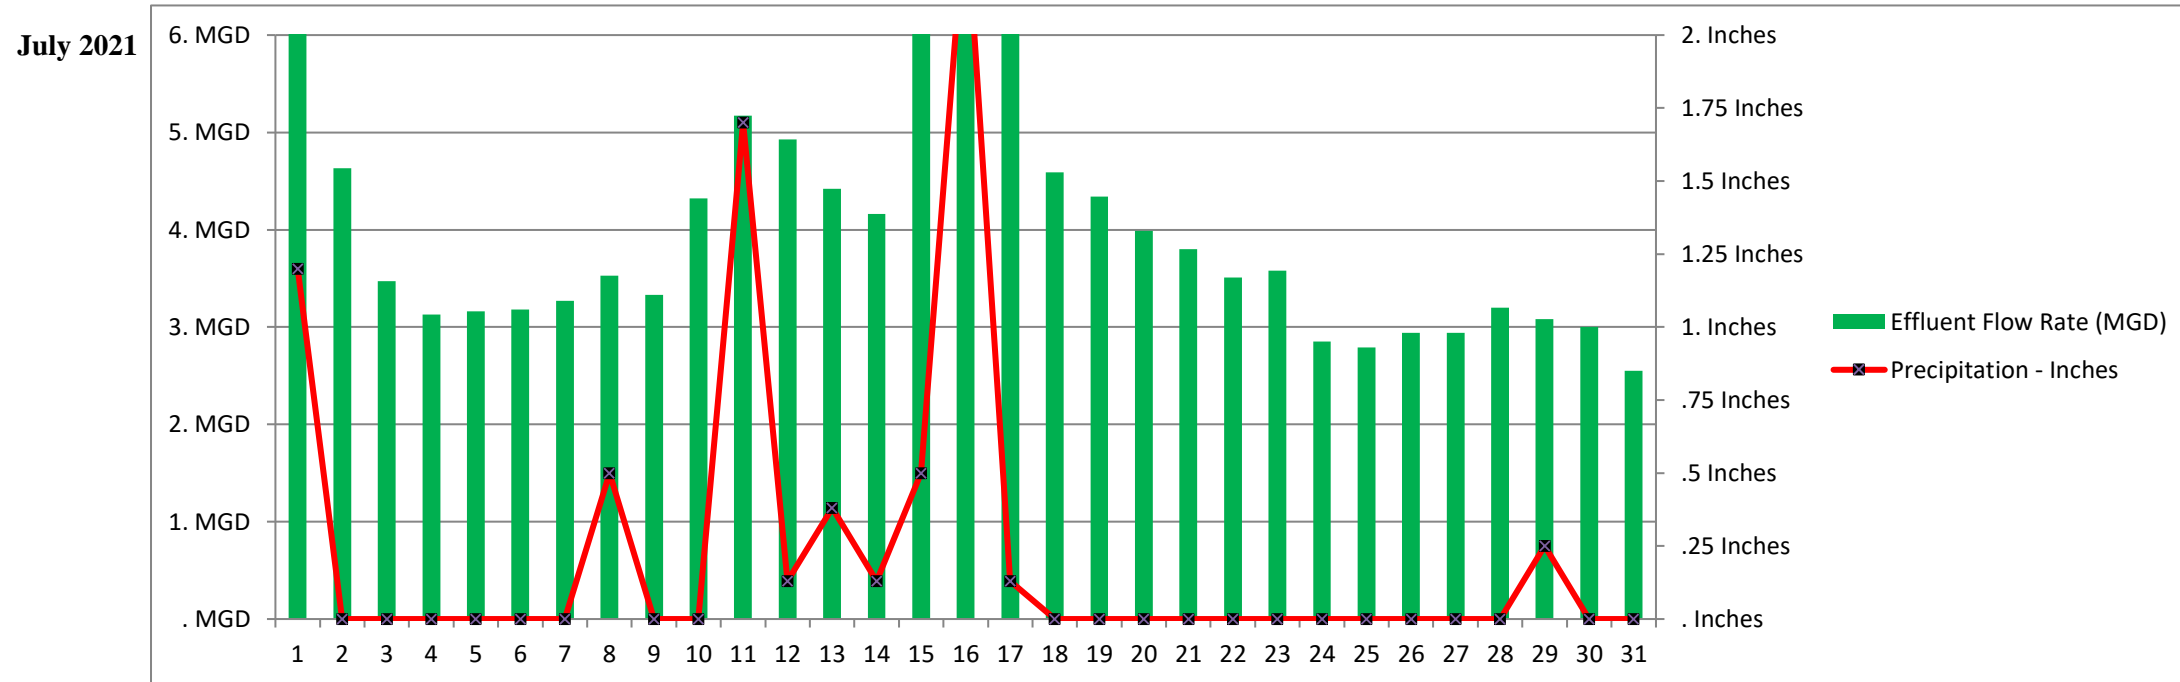

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2021	93.67	91.88	123.06	84.84	99.19	104.57	134.73						731.94
Total MG Treated Effluent 2020	125.83	104.77	110.88	88.40	102.31	95.70	82.61	83.06	64.78	80.31	90.43	83.15	1112.23
Total Monthly Precipitation 2021	2.91	2.53	3.50	3.45	3.41	7.09	7.37						30.26

2021 Monthly Percent Capacity Actual Design Flow 4.0 MGD	76%	82%	99%	71%	80%	87%	109%						86%
---	-----	-----	-----	-----	-----	-----	------	--	--	--	--	--	-----

Sewer Crew Activities	Plant Crew Activities
<ol style="list-style-type: none"> 1. Performed 29 lateral inspections 2. Completed routine maintenance and lift station checks. 3. Cleaned 1980' of sanitary main lines. 4. Responded to 5 sanitary and 4 storm service calls. 5. Fixed wiring at Riley Pool lift station; pulled and cleared debris from pumps. 6. Pump failed in the Windswept Road lift station; need to order a replacement. Installed a back up temporarily. 7. Pulled and cleared pumps at Chapman and Waterview lift stations. 8. Added rip rap to sides of ditch near new access road. 9. Installed 96' of storm pipe, 1 catch basin and a small drain off Pratt St 10. Removed stumps and graded swale in easement at 111 W. Michigan to improve drainage. 	<p style="text-align: center;">Sludge Pressed / Gallons: 849,000</p> <p>Plant Operations and Maintenance:</p> <ol style="list-style-type: none"> 1. Completed required monthly maintenance. 2. Hauled out 63 tons of bio-solids. 3. Replace air compressor for Acti-Flow polymer system. 4. Blower #1 wire connections failed and melted inside the junction box on the motor; replaced wiring with assistance from P&L. 5. Replaced run control timer on cyclone auger in headworks building. 6. Drained, cleaned, and inspected Primary clarifier #3; will return to service once repair parts have been installed (waiting for them to arrive). 7. New access drive is complete, except for a couple items (sidewalk repair and clean up).
