


Wastewater Utility 2021 Monthly Report



November 2021

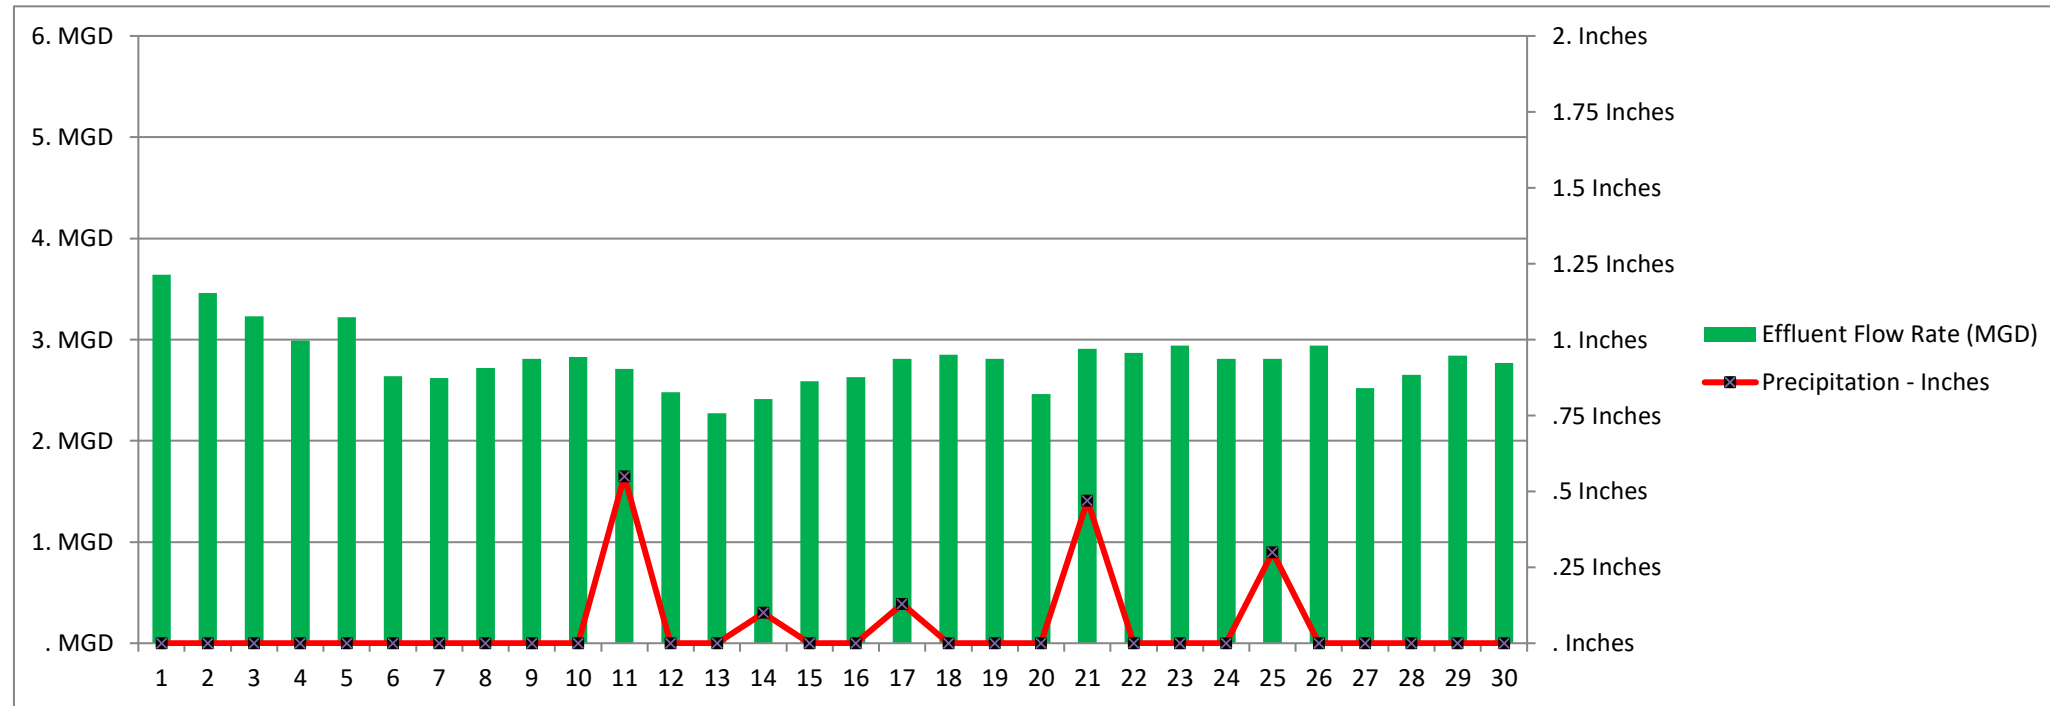

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2021	93.67	91.88	123.06	84.84	99.19	104.57	134.73	79.89	90.88	113.92	84.24		1100.87
Total MG Treated Effluent 2020	125.83	0.00	110.88	88.40	102.31	95.70	82.61	83.06	64.78	80.31	90.43	83.15	1007.46
Total Monthly Precipitation 2021	2.91	2.53	3.50	3.45	3.41	7.09	7.37	2.43	5.81	6.53	1.55		46.58

2021 Monthly Percent Capacity Actual Design Flow 4.0 MGD	76%	82%	99%	71%	80%	87%	109%	64%	76%	92%	70%		82%
---	-----	-----	-----	-----	-----	-----	------	-----	-----	-----	-----	--	-----

Sewer Crew Activities	Plant Crew Activities
<ol style="list-style-type: none"> 1. Performed 24 lateral inspections 2. Completed routine maintenance and lift station checks. 3. Installed 520' of pipe and completed 8 lateral hook ups in McClellan. 4. Responded to 1 sanitary service call. 5. Back up pump at Box Factory failed and had to be changed out again. Also had to replace the level sensor/multi-trode. 6. Replaced the seal fail sensor in one of the Waterview pumps. 7. Small pump station at 1221 E. US 40 failed; changed out and wired in new one. 8. Installed a new catch basin in the easement in McClellan to improve drainage. 9. Cleaned catch basins. 	<p style="text-align: center;">Sludge Pressed / Gallons: 798,900</p> <p>Plant Operations and Maintenance:</p> <ol style="list-style-type: none"> 1. Completed required monthly maintenance. 2. Hauled out 154 tons of bio-solids. 3. Winterized plant stand by generator. 4. Shut down, flushed, and winterized the effluent disinfection system. 5. Repaired RTU 100 in the headworks control panel: power supply issue. 6. Adjusted/tightened blower couplings on digester blowers to stop air leaks. 7. Installed new VFD cooling fan for the digester blowers. 8. Winterized all buildings.
